

# The Village at Downtown


Plumbing Demo

8310 Southwestern Boulevard Dallas, Texas 75206

Date Mon 08/01/2022

Job # 100987

Prepared By Aaron Eagle

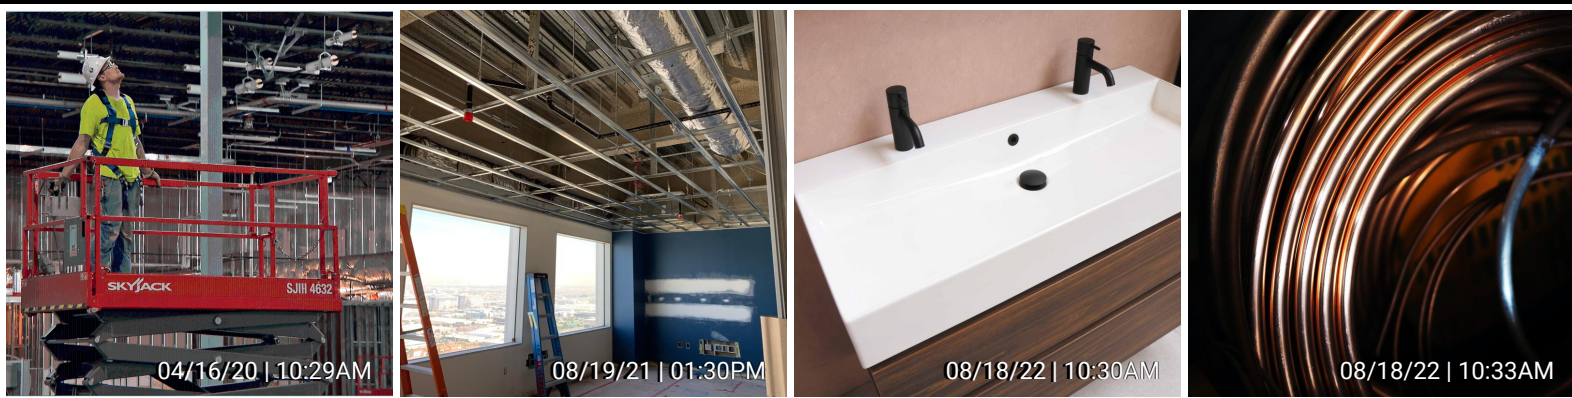

## Weather

6:00 AM	12:00 PM	4:00 PM
<p><b>83°</b> </p> <p>Partially cloudy</p> <p>Wind: 10 MPH   Precipitation: .0"   Humidity: 60%</p>	<p><b>93°</b> </p> <p>Partially cloudy</p> <p>Wind: 4 MPH   Precipitation: .0"   Humidity: 42%</p>	<p><b>99°</b> </p> <p>Partially cloudy</p> <p>Wind: 8 MPH   Precipitation: .0"   Humidity: 33%</p>

## Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Finish Crew	Final caulking sinks on 1st floor restrooms <small>Aaron Eagle   8/18/22 10:18 AM</small>	3	24	<b>24</b>
Piping Crew	Installing domestic hot and cold water lines from 3rd floor riser to Ceiling space. <small>Aaron Eagle   8/22/22 6:15 PM</small>	4	34	<b>34</b>
<b>Total</b>		<b>7</b>	<b>58</b>	<b>58</b>

## Time Cards

Worker	Hours	Pay Type	Classification	Shift	Cost Code	Day Total	Hours To Date	
Finish Crew	<b>Alexandra Guadalupe</b> <small>Plumber PAYROLL ATTACHMENTS:</small>	8	Regular Time	Journeyman	Day Shift	<b>4200</b> <small>Plumbing Fixtures</small>	<b>8</b>	<b>8</b>
	<b>Alfred Gibson</b> <small>Plumber PAYROLL ATTACHMENTS:</small>	8	Regular Time	Journeyman	Day Shift	<b>4200</b> <small>Plumbing Fixtures</small>	<b>8</b>	<b>8</b>
	<b>Algon Walker</b> <small>Plumber PAYROLL ATTACHMENTS:</small>	8	Regular Time	Apprentice	Day Shift	<b>4200</b> <small>Plumbing Fixtures</small>	<b>8</b>	<b>8</b>




Piping Crew

<b>Aaron Eagle</b> Plumber PAYROLL ATTACHMENTS:	8	Regular Time	Foreman	Day Shift	1000 Plumbing Piping	8.5	8.5
	0.5	Overtime	Foreman	Day Shift	1000 Plumbing Piping		
<b>Adrian Cummings</b> Plumber PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	1000 Plumbing Piping	8.5	8.5
	0.5	Overtime	Journeyman	Day Shift	1000 Plumbing Piping		
<b>Aguid Vasconez</b> Plumber PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice	Day Shift	1000 Plumbing Piping	8.5	8.5
	0.5	Overtime	Apprentice	Day Shift	1000 Plumbing Piping		
<b>Alan Chong</b> Plumber PAYROLL ATTACHMENTS:	0.5	Overtime	Journeyman	Day Shift	1000 Plumbing Piping	8.5	8.5
	8	Regular Time	Journeyman	Day Shift	1000 Plumbing Piping		

<b>Total</b>						<b>58</b>	<b>58</b>
--------------	--	--	--	--	--	-----------	-----------

## Work Log Photos

**Piping Crew:** | QTY: 4 | HRS: 34.0 | HTD: 34.0 ↶

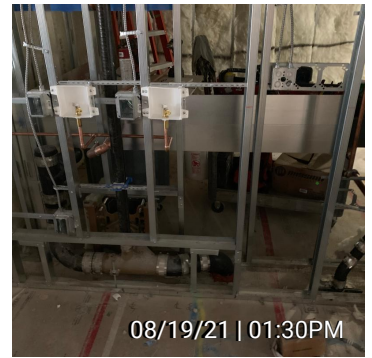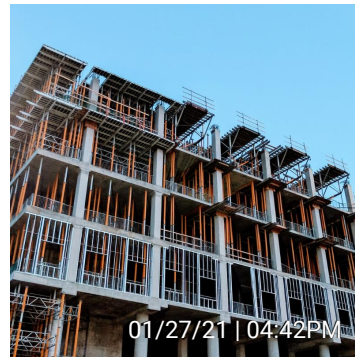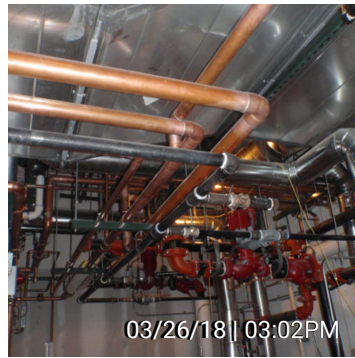

## Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date	Budgeted	% Complete
<b>3/4" Copper Piping</b>	1000 Plumbing Piping	120 lf	120 lf	120 lf	4000 lf	3%
Aaron Eagle   08/18/22   10:35AM						
<b>Sinks</b>	4200 Plumbing Fixtures	6 ea	6 ea	6 ea	20 ea	30%
Aaron Eagle   08/18/22   10:35AM						




## Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
<b>Pipe Cutter</b> 4728		0		1
<b>Scissor Lift</b> 38178		0		1

## General Notes

- GC Asked if we could provide water pumps for basement in anticipation of upcoming storm.

Aaron Eagle | 08/22/22 | 06:18PM

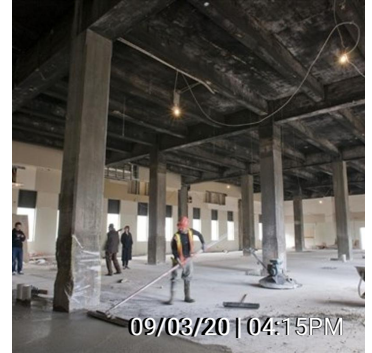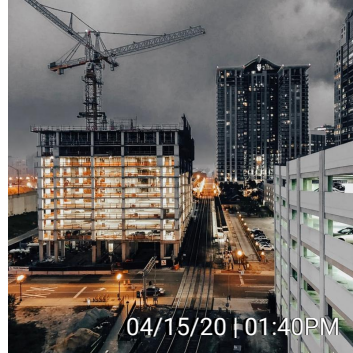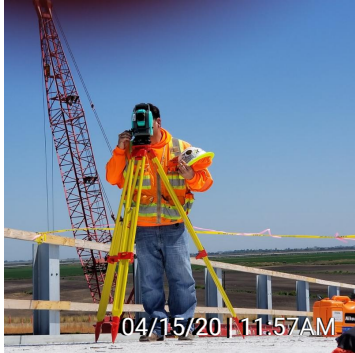

## Site Safety Observations

- Electrical subcontractor kept moving our pipe off the rack and onto the floor creating a back strain and tripping issue.

Aaron Eagle | 08/18/22 | 10:19AM

## Quality Control Observations

- Restroom vanities are missing holes for plumbing hardware. We have to drill the holes ourselves according to GC.

Aaron Eagle | 08/18/22 | 10:19AM

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

Restroom 103 can't be completed because the tile subcontractor isn't completed with the wainscot.

Aaron Eagle | 08/18/22 | 10:34AM

6. Any equipment rented on site?

Scissor Lift

Aaron Eagle | 08/18/22 | 10:34AM

AE

---

I, Aaron Eagle, have reviewed and completed this report.

Aaron Eagle | 08/18/22 | 10:34AM
