

The Village at Downtown





8310 Southwestern Boulevard Dallas, TX 75206



Date Fri 07/28/2023

Job # 12345

Prepared By Daniel Boone

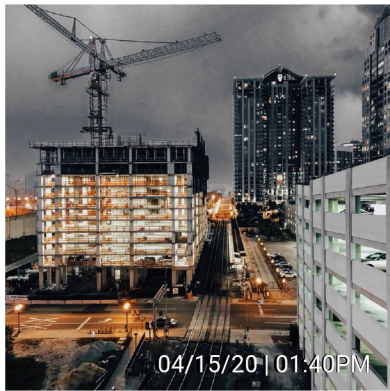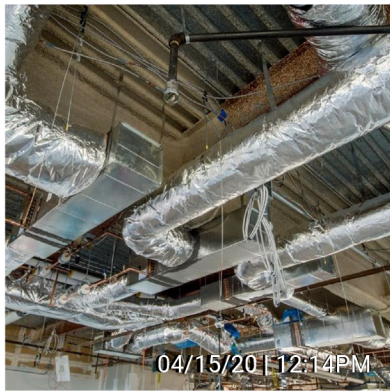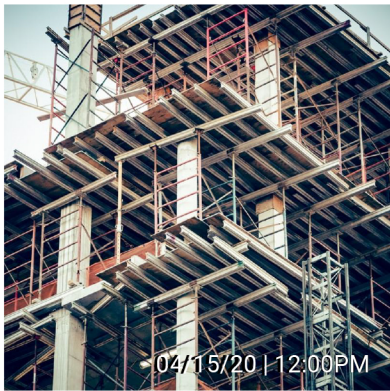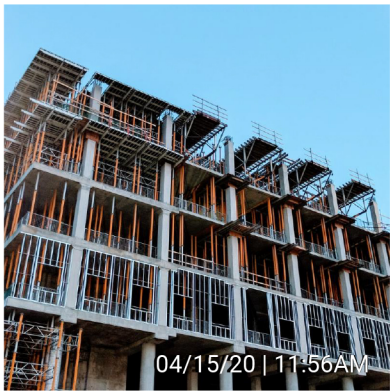

Weather

6:00 AM

83°

Partially cloudy

Wind: 7 MPH | Precipitation: .0" | Humidity: 59%

12:00 PM

94°

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 39%

4:00 PM

99°

Partially cloudy

Wind: 10 MPH | Precipitation: .0" | Humidity: 28%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Level 3 Mechanical Crew	Finished overhead rough-in on level 3. Rough inspection scheduled for tomorrow. Apprentices doing QC to confirm all duct is installed per plan. Team confirmed that all trunk lines and branch lines are in per plan and documented with photos. Framers complete with their scope. They will send this report to the PM for reference. This crew will head to level 4 tomorrow to help with rough-in on that floor. <small>Brad Brennan @Raken 7/26/23 11:14 AM</small>	3	22	94
Level 4 Mechanical Crew	Worked on running main trunk lines overhead and branch lines in the apartments. Rough inspection is scheduled for next week on this floor. Framers are staying ahead but we need a few walls framed on the south side so we can move to that area tomorrow. Electrical crew is on the floor running their conduit and laying out their light fixtures. We walked with their lead and discovered some layout conflicts and issued an RFI to the GC/design team. <small>Brad Brennan @Raken 7/26/23 11:16 AM</small>	6	48	192
Total		9	70	733.25

Time Cards

	Worker	Hours	Pay Type	Classification	Shift	Cost Code	Day Total	Hours To Date
Level 3 Mechanical Crew	Clay Pierce Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice		100-003 Level 3 Mechanical Scope	8	32
	Dean Martinez Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice		100-003 Level 3 Mechanical Scope	8	40
	Gary Bushnell Journeyman PAYROLL ATTACHMENTS:	6	Regular Time	Journeyman		100-003 Level 3 Mechanical Scope	6	46
Level 4 Mechanical Crew	John Hess Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman		100-004 Level 4 Mechanical Scope	8	40
	Luis Alvarado Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman		100-004 Level 4 Mechanical Scope	8	48
	Nick Ramirez Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice		100-004 Level 4 Mechanical Scope	8	40
	Ricky Wyatt Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman		100-004 Level 4 Mechanical Scope	8	40
	Tim Jones Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice		100-004 Level 4 Mechanical Scope	8	40
	Walter Wilson Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice		100-004 Level 4 Mechanical Scope	8	40
Total							70	398


Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date	Budgeted	% Complete
24"Main Duct Received main duct for level 3. Brad Brennan @Raken 07/27/23 04:16PM	100-003 Level 3 Mechanical Scope	250 lf	250 lf	250 lf	250 lf	100%
8"Round Duct Received delivery of 8" round duct for level 4. Brad Brennan @Raken 07/27/23 04:04PM	100-004 Level 4 Mechanical Scope	75 lf	75 lf	140 lf	150 lf	93.33%

8"Round Duct 100-003 Level 3 Mechanical Scope Received delivery of 8" round duct for level 3. Brad Brennan @Raken 07/27/23 04:03PM	150	150	195	300	65%
EVAPs 100-003 Level 3 Mechanical Scope Installed 2 EVAPs in NW quadrant Daniel Boone 08/01/23 04:27PM	2	2	2	0	0%


Equipment					
Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site	
Scissor Lift 003	United Rentals	7	Screws removed from wheels Daniel Boone 08/01/23 04:23PM	5	
Scissor Lift 002	United Rentals	8	Cleaned at end of shift Daniel Boone 08/01/23 04:23PM	8	
Scissor Lift 001	United Rentals	0		8	

General Notes	
1. New delivery of ductwork for level 5 arrived at 5 AM. We used the forklift to unload it and brought it to our staging area. Delivery took about 2 hours to unload and stage. Apprentices will start running this duct up to levels 4 and 5 tomorrow morning to finish level 4 rough-in and prepare for level 5 rough-in. Brad Brennan @Raken 07/26/23 12:00AM	

Site Safety Observations	
1. We hosted a crew meeting at 6 AM to discuss safety protocols on the project and ensure everyone is on the same page. Brad Brennan @Raken 07/26/23 12:00AM	
 04/15/20 01:17PM	 04/15/20 01:18PM
 04/15/20 01:18PM	 09/03/20 04:11PM




Quality Control Observations	
1. Apprentices walked around level 3 to confirm that all trunks lines are in per plan before our overhead rough inspection tomorrow. Drywallers are scheduled to start hanging the next day. Brad Brennan @Raken 07/26/23 12:00AM	

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur? 	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<p>During layout on level 4 we discovered conflicts with main trunk lines and light fixtures in the corridor. An RFI was written and we are waiting on response from design team before proceeding any further.</p> <p>Daniel Boone 06/03/20 01:30PM</p>
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<p>Safety Manager walked the site to review our crews and the project.</p> <p>Daniel Boone 06/03/20 01:31PM</p>
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<p>Level 4 is on hold.</p> <p>Daniel Boone 06/03/20 01:31PM</p>
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<p>Scissor lifts and fork lift.</p> <p>Daniel Boone 06/03/20 01:31PM</p>

Survey Photos

2. 

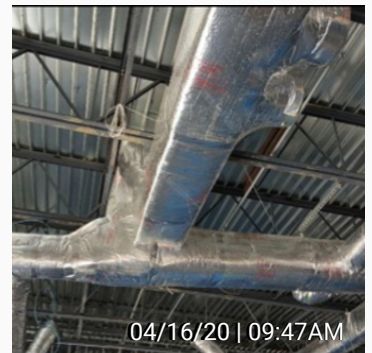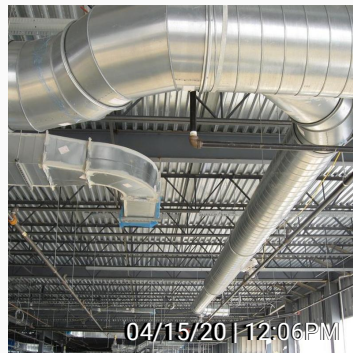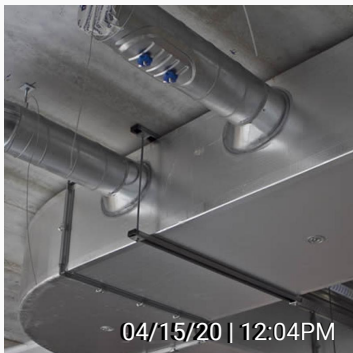



I, Daniel Boone, have reviewed and completed this report.

Daniel Boone | 08/01/23 | 04:27PM
