

The Village at Downtown



Painting PDF

8310 Southwestern Boulevard Dallas, Texas 75206

Date Mon 05/15/2023

Job # 12345

Prepared By Aaron Eagle

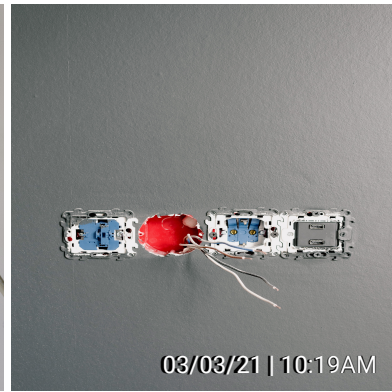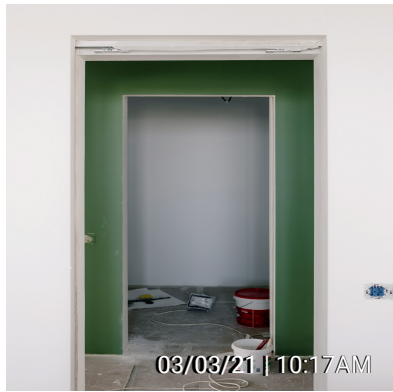

Weather

6:00 AM

67°

Partially cloudy

Wind: 4 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

81°

Partially cloudy

Wind: 6 MPH | Precipitation: .0" | Humidity: 67%

4:00 PM

74°

Rain, Partially cloudy

Wind: 6 MPH | Precipitation: .11" | Humidity: 83%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Andre Marshall	"Pre-punch list" touch up on first floor walls and soffits where finish trim was installed on east side. Completed list of items captured by GC Superintendent and our PM based on their walk last week. <small>Nick Pettengill @Raken 5/11/23 3:46 PM</small>	1	8	8
Anti-Graffiti	Painting Columns in parking garage with anti-graffiti paint. Coordinated with electrician to move his material away from columns we plan to paint tomorrow. <small>Nick Pettengill @Raken 5/13/23 3:40 PM</small>	3	18	18
Finish Crew	Painted final coat on ceilings on 2nd floor (entire floor footprint). Starting mobilizing to the 3rd floor at end of day to prepare for starting up there tomorrow. <small>Nick Pettengill @Raken 5/13/23 1:22 PM</small>	4	32	230
Paint Crew	Prime and first coat walls and soffits on 3rd floor hallways and east half of available private apartments. <small>Nick Pettengill @Raken 5/13/23 1:21 PM</small>	6	48	236
Total		14	106	508

Time Cards

Worker	Hours	Pay Type	Classification	Shift	Cost Code	Day Total	Hours To Date
--------	-------	----------	----------------	-------	-----------	-----------	---------------

Andre Marshall

Andre Marshall Carpenter PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	9100-01 Level 1 Paint	8	8
--	---	--------------	------------	-----------	--------------------------	---	---

Anti-Graffiti

Alfred Lala Apprentice PAYROLL ATTACHMENTS:	6	Regular Time	Apprentice	Day Shift	9620-01 Graffiti Resistant Paint	6	6
Algon Walker Journeyman PAYROLL ATTACHMENTS:	6	Regular Time	Journeyman	Day Shift	9620-01 Graffiti Resistant Paint	6	6
Allen Williams Journeyman PAYROLL ATTACHMENTS:	6	Regular Time	Journeyman	Day Shift	9620-01 Graffiti Resistant Paint	6	6

Finish Crew

Albert Delia Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	9100-02 Level 2 Paint	8	41
Alexander Cea Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	9100-02 Level 2 Paint	8	41
Alexandra Guadalupe Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice	Day Shift	9100-02 Level 2 Paint	8	41
Alexandre DeSousa Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice	Day Shift	9100-02 Level 2 Paint	8	41

Paint Crew

Aaron Eagle Foreman PAYROLL ATTACHMENTS:	8	Regular Time	Foreman	Day Shift	9100-03 Level 3 Paint	8	36
Adam Carrera Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	9100-03 Level 3 Paint	8	40
Adrian Cummings Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	9100-03 Level 3 Paint	8	40
Agostino Valente Journeyman PAYROLL ATTACHMENTS:	8	Regular Time	Journeyman	Day Shift	9100-03 Level 3 Paint	8	40
Aguid Vasconez Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice	Day Shift	9100-03 Level 3 Paint	8	40
Alan Chong Apprentice PAYROLL ATTACHMENTS:	8	Regular Time	Apprentice	Day Shift	9100-03 Level 3 Paint	8	40

Total

106

508

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date	Budgeted	% Complete
Graffiti Resistant Paint	9620-01 Graffiti Resistant Paint	10 gal	10 gal	10 gal	90 gal	11.11%
Nick Pettengill @Raken 05/13/23 03:38PM						
Primer & Finish	9100-03 Level 3 Paint	30 gal	30 gal	100 gal	150 gal	66.67%
Nick Pettengill @Raken 05/13/23 04:46PM						
Primer & Finish	9100-01 Level 1 Paint	5 gal	5 gal	120 gal	150 gal	80%
Nick Pettengill @Raken 05/13/23 03:30PM						
Primer & Finish	9100-02 Level 2 Paint	30 gal	30 gal	140 gal	125 gal	100%
Nick Pettengill @Raken 05/13/23 01:24PM						



Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
Scissor Lift 001		0		8

General Notes

1. Ceilings on 2nd and 3rd floor still being hung and taped by drywall subcontractor - noted here as out of sequence work. Painting PM and GC to discuss reimbursement.

Nick Pettengill @Raken | 05/12/23 | 12:00AM

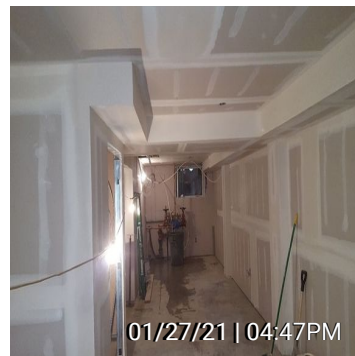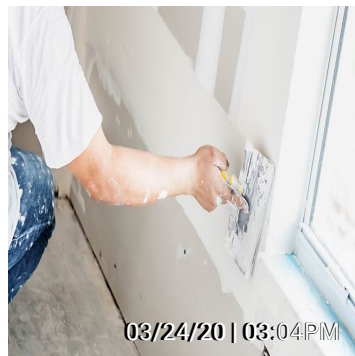

Site Safety Observations

1. Interior Glass installers were using aluminum step ladder. GC was notified that it is unsafe.

Nick Pettengill @Raken | 05/12/23 | 12:00AM

Quality Control Observations

1. Fire sprinkler subcontractor left oily fingerprints at approximately 90% of sprinkler escucion locations. GC was verbally notified of this issue and reminded the sprinkler subcontractor to wear gloves and ensure everything touching the finish painted surface was clean of any oil or residue.

Nick Pettengill @Raken | 05/12/23 | 12:00AM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Yes, an HVAC apprentice got a bit of paint in his eye and had to flush it out at the onsite eyewash station. This is no fault of our own becuase the individual was not wearing his safety glasses in an area that we were actively painting. <small>Aaron Eagle 03/05/21 12:28PM</small>
2. Any schedule delays occur?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Yes, an electrician hit a fire sprinkler head unloading black water in a large apartment on the 2nd floor. Repainting will be required once the room is dried out and cleaned. <small>Aaron Eagle 03/05/21 12:27PM</small>
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	



I, Aaron Eagle, have reviewed and completed this report.

Aaron Eagle | 03/05/21 | 12:28PM
