

The Village at Downtown


8310 Southwestern Boulevard Dallas, TX 75206



Date Thu 03/28/2024

Job # 0212

Prepared By Michael Boone

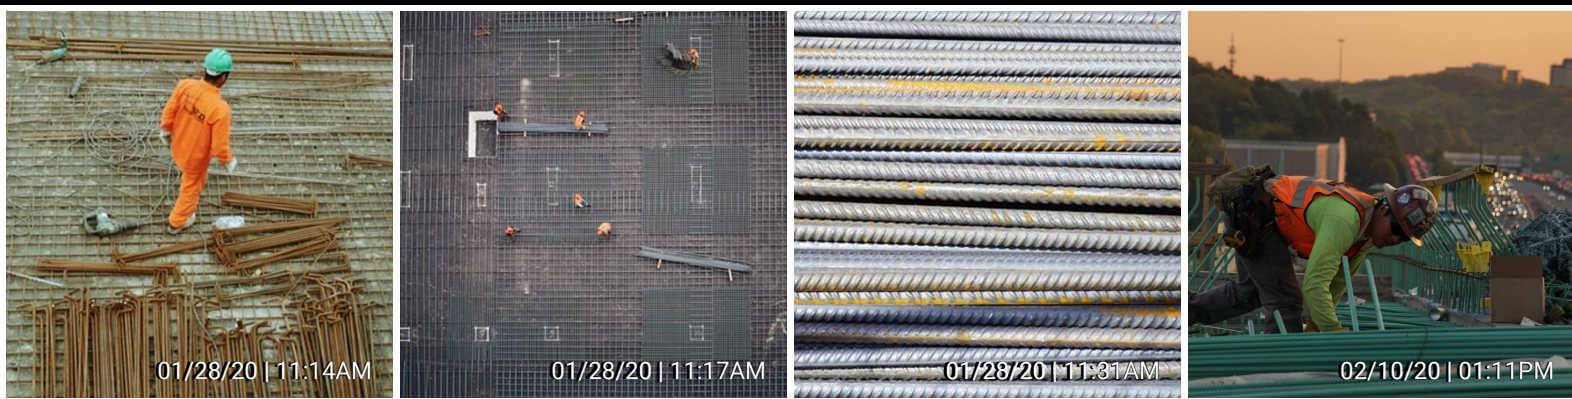

Weather

6:00 AM

45°

Clear

Wind: 1 MPH | Precipitation: .0" | Humidity: 75%

12:00 PM

64°

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 52%

4:00 PM

73°

Partially cloudy

Wind: 7 MPH | Precipitation: .0" | Humidity: 43%

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
Christopher Hardy	Working on rebar for level 3. Leading the rebar crew to ensure that all rebar is installed per plan and that all deliveries are made to meet the schedule. <small>Alissa Rogers @Raken 4/2/24 2:03 PM</small>	1	8	24
Concrete Crew	Poured & finished concrete on level 2. Pour started at 7 AM when trucks rolled up and were finished by 5 PM. <small>Alissa Rogers @Raken 3/30/24 3:19 PM</small>	6	44	246
Kenny Powers	Working on rebar with level 3 crew. Ran the forklift most of the day helping to unload new delivery of rebar and coordinated with Chris to make sure that apprentices got the rebar up to level 3. Coordinating with the tower crane operator. <small>Alissa Rogers @Raken 4/2/24 2:06 PM</small>	1	8	16
Total		8	60	516

Time Cards

Worker	Hours	Pay Type	Classification	Shift	Cost Code	Day Total	Hours To Date	
Christopher Hardy Ironworker PAYROLL ATTACHMENTS:	8	Regular Time	Ironworker		510.0180 Anchor Bolt/Rebar Template	8	32	
Concrete Crew	Antonio Fidalgo Cement Mason PAYROLL ATTACHMENTS:	6	Regular Time	Cement Mason		510.5010 Concrete Stairs	6	24
	Arthur Ferramosca Cement Mason PAYROLL ATTACHMENTS:	6	Regular Time	Cement Mason			6	32
	Christopher Messano Cement Mason PAYROLL ATTACHMENTS:	8	Regular Time	Cement Mason			8	8
	Chis Chirco Cement Mason PAYROLL ATTACHMENTS:	8	Regular Time	Cement Mason			8	8
	Dean Costa Cement Mason PAYROLL ATTACHMENTS:	8	Regular Time	Cement Mason			8	8
	Antonio Fidalgo Laborer PAYROLL ATTACHMENTS:	8	Regular Time	Laborer			8	10
Kenny Powers Carpenter PAYROLL ATTACHMENTS:	8	Regular Time	Carpenter		510.0180 Anchor Bolt/Rebar Template	8	24	
Total						60	516	

Materials						
Material	Cost Code	Day Total	Week Total	Quantities to Date	Budgeted	% Complete
Concrete Concrete Deck on Building A Alissa Rogers @Raken 03/22/24 05:20PM	510.5010 Concrete Stairs	200 cy	200 cy	200 cy	360 cy	55.56%
Concrete Concrete walkway around Building A Alissa Rogers @Raken 03/30/24 03:47PM	510.3030 Hardscape	70 lf	350 lf	350 lf	350 lf	100%
Rebar	510.0180 Anchor Bolt/Rebar Template	400 lf	2200 lf	2200 lf	0 lf	0%



Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
Concrete Boom Pump 345674		0		3
Forklift	United Rentals	0		7

General Notes

1. Rebar was delivered today - arrived at 5am

Alissa Rogers @Raken | 03/27/24 | 12:00AM

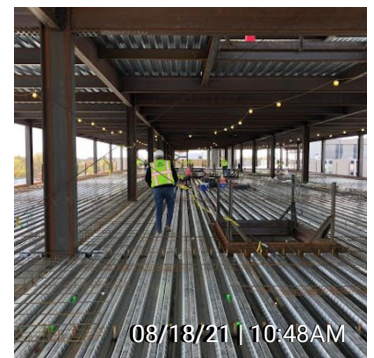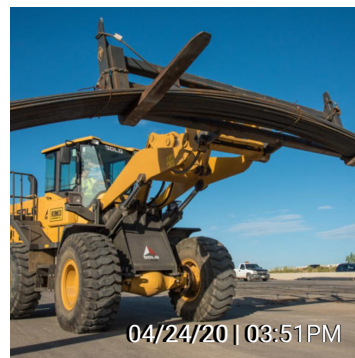

Site Safety Observations

- 1. It appears that someone hit the base of the scaffold at the perimeter of the building when we started our shift today. The crew double checked all connections and the integrity of the base before continuing to erect the second level.**

Alissa Rogers @Raken | 03/28/24 | 12:00AM

Quality Control Observations

- 1. Electricians are running conduit on the bottom of the slab, not between our top and bottom layers. This will have to be redone seeing as the structural engineer will not allow anything other than within the middle third of the deck.**


Alissa Rogers @Raken | 03/28/24 | 12:00AM

Survey

Questions

N/A No Yes Description

1. Any accidents on site today?

2. Any schedule delays occur? 

Only received partial shipment of rebar today so we could not finish the level 3 deck.

Alissa Rogers @Raken | 04/02/24 | 12:55PM

3. Did weather cause any delays?

4. Any visitors on site?

Rebar delivery truck

Alissa Rogers @Raken | 04/02/24 | 12:55PM

5. Any areas that can't be worked on?



6. Any equipment rented on site?

Gradall

Alissa Rogers @Raken | 04/02/24 | 12:55PM

Survey Photos

2. 

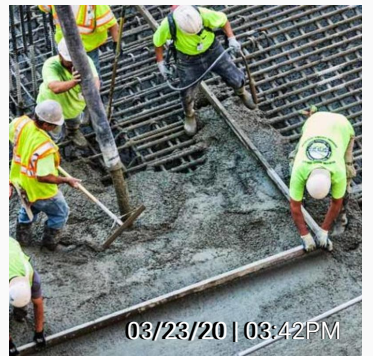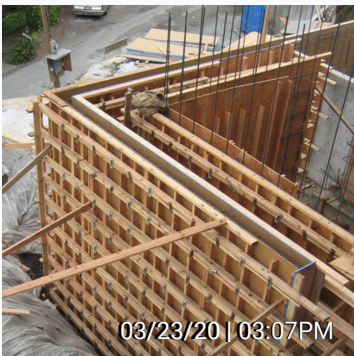

I, Michael Boone, have reviewed and completed this report.

Michael Boone | 04/17/20 | 01:21PM
